

Wakonda Drive Neighborhood Project

October 22, 2015


STREET CLOSURE: Access to Wakonda Drive will be limited for the remainder of this project. Four intersections, hi-lighted in yellow on the picture to the right, will allow traffic access to/from Wakonda Drive. All other intersections will remain closed until the final street paving is complete. We anticipate the final street paving to occur the first week in November.

The intersections that will be closed are receiving full depth asphalt replacement. For this process to happen, the entire surface will be removed and rock installed and compacted. The contractor will lay down the initial base layer of asphalt which will serve as a stabilizer. The final step is to place the surface course of asphalt.

There are approximately eleven different intersections along Wakonda Drive that will go through this process. We understand that this is an additional inconvenience for residents and are hopeful that we can complete this portion of the project as quickly and effectively as possible.

COMMUNICATION: Our goal is to keep everyone up-to-date on the progress of this project. If you have not provided us with your contact information (e-mail address/ phone number), please do so. We would also like to send these updates by e-mail as much as possible.

Please do not hesitate to contact Dan Nixon or Tim Hoskins with any questions or concerns. We will make every effort to get back to you quickly.

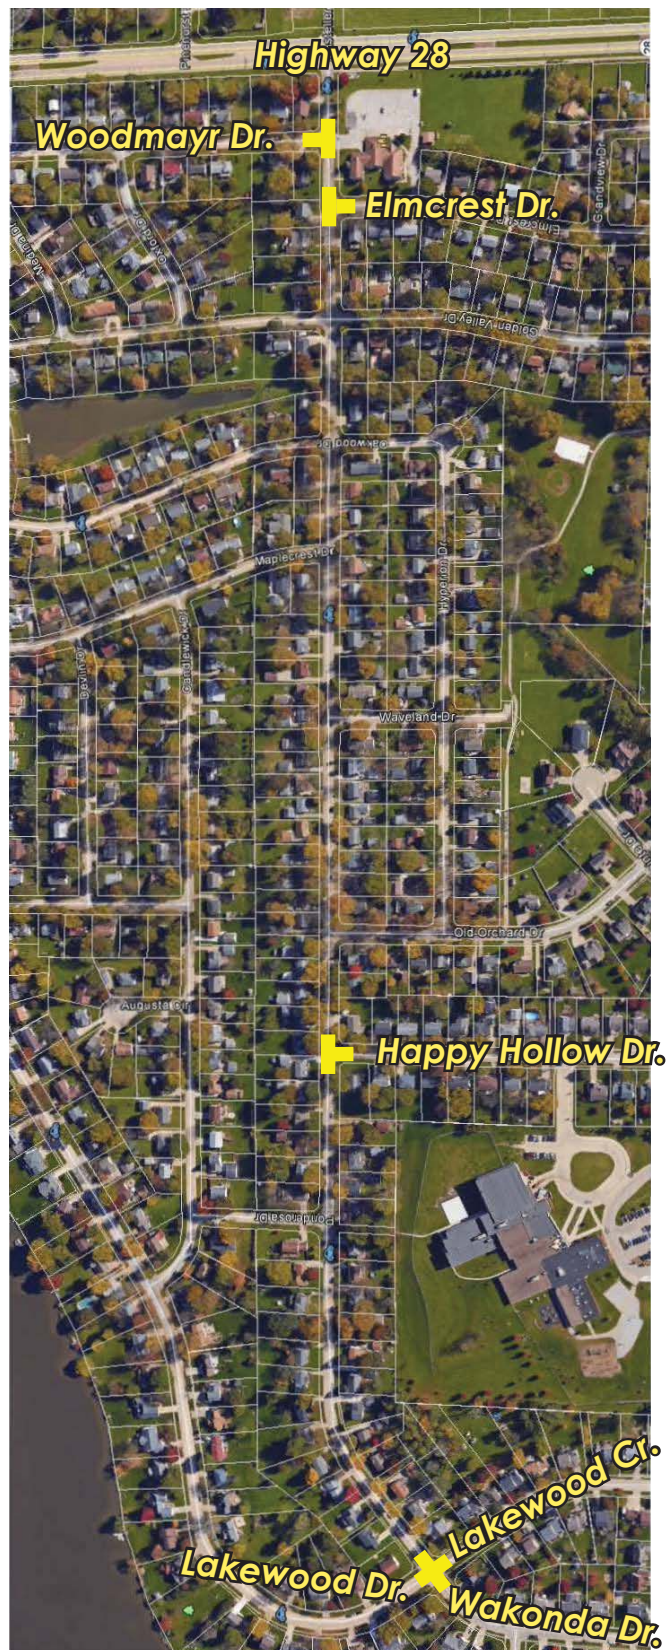

Tim Hoskins
Public Works Director
515.981.9527



Dan Nixon
On-Site Representative
515.979.3837
